



THE UNIVERSITY OF
SYDNEY

Room Number _____

Seat Number _____

Student Number _____

ANONYMOUSLY MARKED

(Please do not write your name on this exam paper)

CONFIDENTIAL EXAM PAPER

This paper is not to be removed from the exam venue

Computer Science

PRACTICE EXAMINATION

Semester 1 - Final, 2026

INFO6007 Project Management in IT

For Examiner Use Only

EXAM WRITING TIME: 2 hours
READING TIME: 10 minutes

EXAM CONDITIONS:

This is a RESTRICTED OPEN book exam - specified materials permitted

MATERIALS PERMITTED IN THE EXAM VENUE:

(No electronic aids are permitted e.g. laptops, phones)

One A4 sheet of handwritten and/or typed notes double-sided
Bilingual dictionary

MATERIALS TO BE SUPPLIED TO STUDENTS:

1 x 16-page answer book

Answer sheet: Gradescope MCQ (double-sided - 200 Qs)

Blank scratch paper (1 sheet; more may be provided upon student request)

INSTRUCTIONS TO STUDENTS:

Please tick the box to confirm that your examination paper is complete. ☐

Q	Mark
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	

Total _____

Section 1: Multiple Choice Questions (10 Marks)

Note: Each question carries 1 mark. Only one answer is correct (10 Marks)

Question 1: Which of the following is a defining feature of a project?

- a) Repetitive daily operations
- ☒ b) Produces a unique outcome
- c) Runs indefinitely
- d) Requires minimal planning

Question 2: The triple constraint in project management is commonly represented as:

- a) Cost, Scope, Quality
- ☒ b) Scope, Time, Cost
- c) Risk, Resources, Communication
- d) Time, Quality, Communication

Question 3: In Scrum, a set period during which work is completed and reviewed is called:

- a) Milestone
- ☒ b) Iteration (Sprint)
- c) Phase
- d) Task

Question 4: Which scheduling tool visually shows tasks along a timeline but does not explicitly display dependencies?

- ☒ a) Gantt Chart
- b) PERT Chart
- c) Activity on Node (AON)
- d) RACI Matrix

Question 5: Actual Cost (AC) represents:

- a) Budgeted value of work performed
- b) Planned value of scheduled work
- ☒ c) Money actually spent to perform the work
- d) Estimate to complete remaining work

Question 6: Which is a quantitative risk analysis technique?

- a) Probability and Impact Matrix
- b) Delphi Technique
- ☒ c) Monte Carlo Simulation
- d) Brainstorming

Question 7: In procurement, an RFP (Request for Proposal) is most appropriate when:

- a) Price is the sole deciding factor
- ☒ b) Detailed solutions and vendor creativity are required
- c) Scope is very clear and fixed

d) Long-term supplier relationships are irrelevant

? C Question 8: Which leadership style relies on reward and punishment to manage team performance?

- a) Transformational X
- b) Servant X
- c) Transactional
- d) Laissez-faire X

Question G: Which of the following is NOT a standard project lifecycle phase?

- a) Initiation
- b) Planning
- ✓ c) Operation
- d) Closure

Question 10: Which tool is used to identify roles, responsibilities, and accountability for project tasks?

- a) WBS
- ✓ b) RACI Matrix
- c) Gantt Chart
- d) PERT Chart

Section 2 - Questions based on Scenarios (40 Marks)

Question 11

12 Marks

You are managing a project to deploy a smart city traffic management system. The simplified schedule includes:

Activity P: 3 days, complete

Activity Q: 5 days, depends on P


Activity R: 4 days, depends on P


Activity S: 6 days, depends on both Q and R

Activity T: 2 days, depends on S

Some tasks are slightly over budget and behind schedule.

- a) Identify the critical path and total expected project duration. Explain your reasoning. (4 Marks)

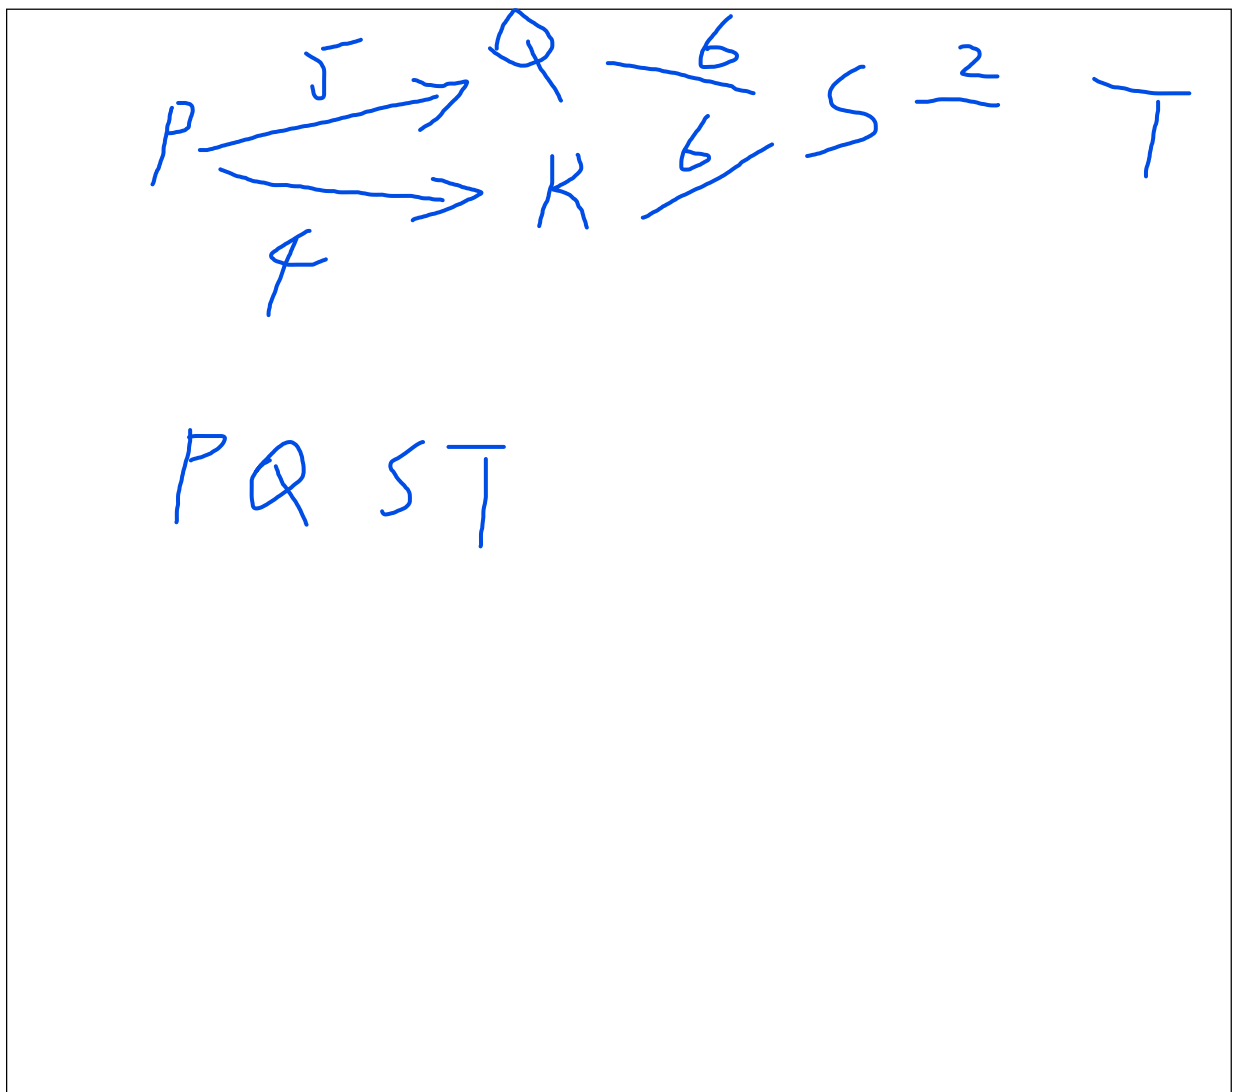




- b) The project team reports that Activity Q and Activity S are taking longer than expected, and some work packages are using more resources than planned. Explain how this may affect the overall project schedule and budget. Suggest one practical action the project manager should take to bring the project back under control. (Refer to the Question 11 scenario)
(5 Marks)

- c) Create a three-level WBS for the traffic management system, including at least two major deliverables and their subcomponents. (Refer to the Question 11 scenario)
(5 Marks)

Question 12**12 Marks**

Your team is developing an e-learning platform for a university using Agile. Midway through a sprint, the dean requests new features for accessibility compliance, creating tension with the team regarding deadlines.

- a) Explain why managing stakeholder expectations can be more complex in Agile than in Waterfall, using this scenario. (5 Marks)



- b) Suggest two strategies the project team could implement to manage mid-sprint changes effectively. (Refer to the Question 12 scenario) (4 Marks)


- c) Draft one example clause for the project charter specifying how scope changes will be handled in this Agile project. (Refer to the Question 12 scenario) (4 Marks)

Question 13

11 Marks


Your IT project team includes senior engineers and junior trainees. Conflict arises because juniors feel unheard, while seniors feel pressured to maintain deadlines.

- a) Identify the most suitable conflict resolution style for this situation and justify your choice. (4 Marks)



- b) Using Maslow's Hierarchy of Needs Theory, explain why the juniors may feel disengaged. (Refer to the Question 13 scenario) (5 Marks)**

- c) Suggest two leadership practices to restore team cohesion and improve morale.
(Refer to the Question 13 scenario) (4 Marks)



END OF EXAMINATION
