

INFO6007

Project Management in IT

Week 13 – Semester review and Final exam prep


Semester 1, 2026



Acknowledgement of Country

I would like to acknowledge the Traditional Owners of Australia and recognise their continuing connection to land, water and culture. I am currently on the land of the Gadigal people of the Eora nation and pay my respects to their Elders, past, present and emerging.

I further acknowledge the Traditional Owners of the country on which you are on and pay respects to their Elders, past, present and future.



Copyright Warning

COMMONWEALTH OF AUSTRALIA

Copyright Regulations 1969

WARNING


This material has been reproduced and communicated to you by or on behalf of the University of Sydney pursuant to Part VB of the Copyright Act 1968 (**the Act**).

The material in this communication may be subject to copyright under the Act. Any further copying or communication of this material by you may be the subject of copyright protection under the Act.

Do not remove this notice.

Reminder of the Knowledge Areas

Knowledge Area 1 – Stakeholder Management

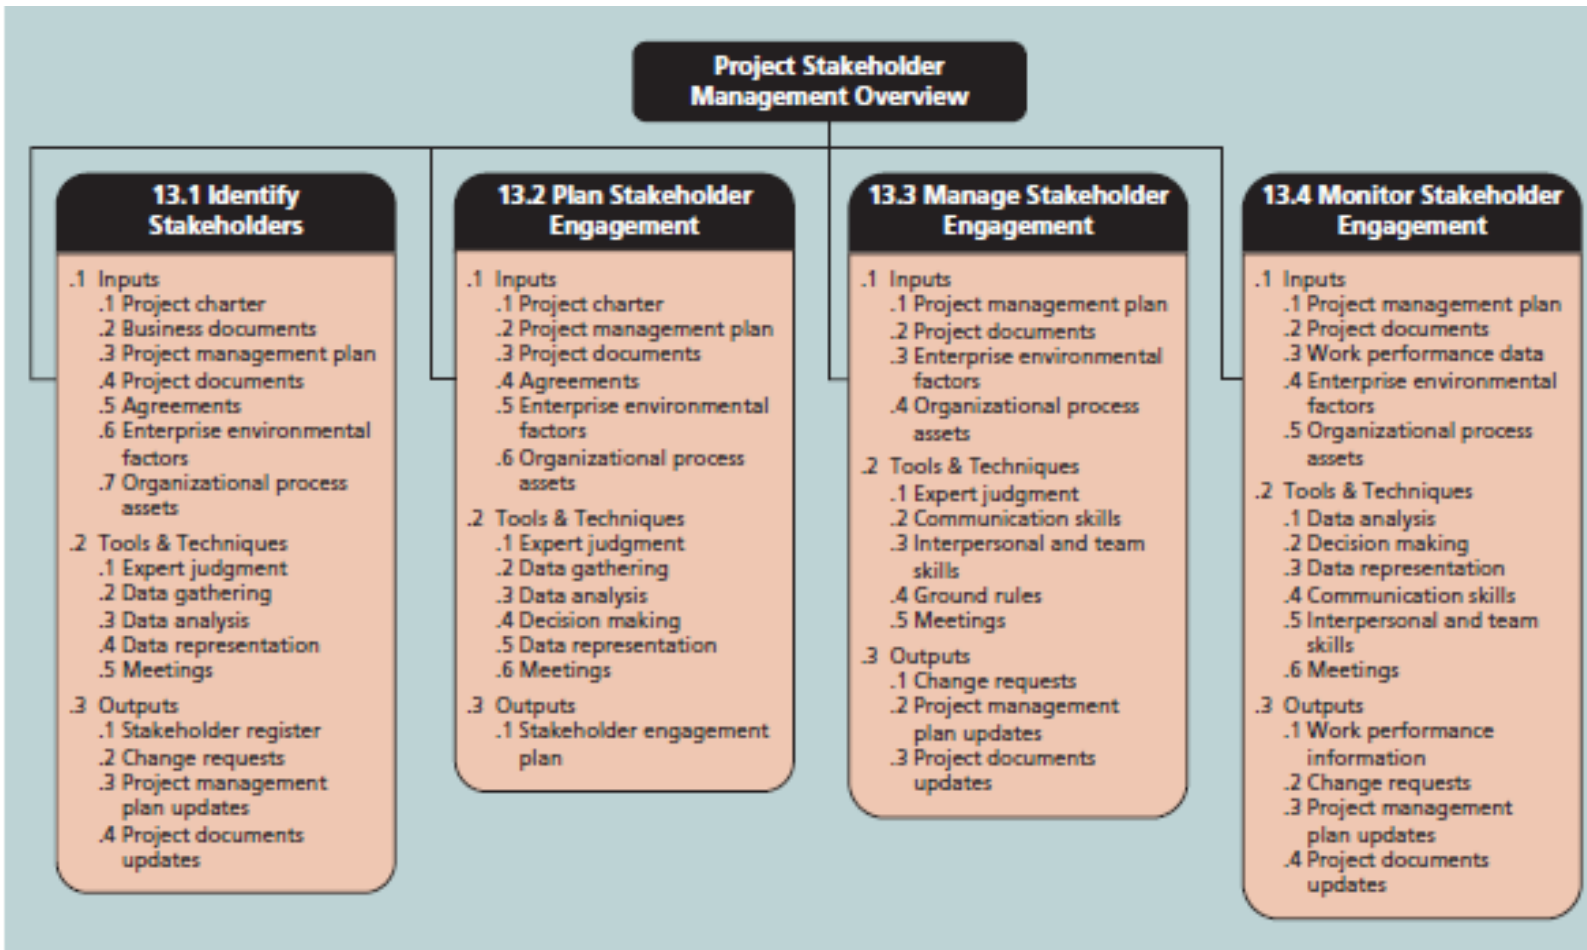

- **Purpose:** Identify, engage, and manage stakeholders to meet expectations.
- **Key activities:** Identify stakeholders, plan engagement, manage engagement, monitor engagement.
- **IT example:** Ensuring business users, IT teams, and vendors are aligned on system requirements.

Source: *PMBOK® Guide – Sixth Edition*. Project Management Institute, Inc. (2017). Copyright and all rights reserved. Material from this publication has been reproduced with permission of PMI.

Project Scope Management Overview

5.1 Plan Scope Management

- .1 Inputs
 - .1 Project charter
 - .2 Project management plan
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data analysis
 - .3 Meetings
- .3 Outputs
 - .1 Scope management plan
 - .2 Requirements management plan

5.4 Create WBS

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Decomposition
- .3 Outputs
 - .1 Scope baseline
 - .2 Project documents updates

5.2 Collect Requirements

- .1 Inputs
 - .1 Project charter
 - .2 Project management plan
 - .3 Project documents
 - .4 Business documents
 - .5 Agreements
 - .6 Enterprise environmental factors
 - .7 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data gathering
 - .3 Data analysis
 - .4 Decision making
 - .5 Data representation
 - .6 Interpersonal and team skills
 - .7 Context diagram
 - .8 Prototypes
- .3 Outputs
 - .1 Requirements documentation
 - .2 Requirements traceability matrix

5.5 Validate Scope

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Verified deliverables
 - .4 Work performance data
- .2 Tools & Techniques
 - .1 Inspection
 - .2 Decision making
- .3 Outputs
 - .1 Accepted deliverables
 - .2 Work performance information
 - .3 Change requests
 - .4 Project documents updates

5.3 Define Scope

- .1 Inputs
 - .1 Project charter
 - .2 Project management plan
 - .3 Project documents
 - .4 Enterprise environmental factors
 - .5 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data analysis
 - .3 Decision making
 - .4 Interpersonal and team skills
 - .5 Product analysis
- .3 Outputs
 - .1 Project scope statement
 - .2 Project documents updates

5.6 Control Scope

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Work performance data
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Data analysis
- .3 Outputs
 - .1 Work performance information
 - .2 Change requests
 - .3 Project management plan updates
 - .4 Project documents updates

Knowledge Area 2 - Scope Management

- **Purpose:** Defines what is included and excluded from the project.
- **Key activities:** Collect requirements, define scope, create WBS, validate and control scope.
- **IT example:** Determining features for a new software module without exceeding project boundaries.

Project Schedule Management Overview

6.1 Plan Schedule Management

- .1 Inputs
 - .1 Project charter
 - .2 Project management plan
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data analysis
 - .3 Meetings
- .3 Outputs
 - .1 Schedule management plan

6.4 Estimate Activity Durations

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Analogous estimating
 - .3 Parametric estimating
 - .4 Three-point estimating
 - .5 Bottom-up estimating
 - .6 Data analysis
 - .7 Decision making
 - .8 Meetings
- .3 Outputs
 - .1 Duration estimates
 - .2 Basis of estimates
 - .3 Project documents updates

6.2 Define Activities

- .1 Inputs
 - .1 Project management plan
 - .2 Enterprise environmental factors
 - .3 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Decomposition
 - .3 Rolling wave planning
 - .4 Meetings
- .3 Outputs
 - .1 Activity list
 - .2 Activity attributes
 - .3 Milestone list
 - .4 Change requests
 - .5 Project management plan updates

6.5 Develop Schedule

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Agreements
 - .4 Enterprise environmental factors
 - .5 Organizational process assets
- .2 Tools & Techniques
 - .1 Schedule network analysis
 - .2 Critical path method
 - .3 Resource optimization
 - .4 Data analysis
 - .5 Leads and lags
 - .6 Schedule compression
 - .7 Project management information system
 - .8 Agile release planning
- .3 Outputs
 - .1 Schedule baseline
 - .2 Project schedule
 - .3 Schedule data
 - .4 Project calendars
 - .5 Change requests
 - .6 Project management plan updates
 - .7 Project documents updates

6.3 Sequence Activities

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Precedence diagramming method
 - .2 Dependency determination and integration
 - .3 Leads and lags
 - .4 Project management information system
- .3 Outputs
 - .1 Project schedule network diagrams
 - .2 Project documents updates

6.6 Control Schedule

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Work performance data
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Data analysis
 - .2 Critical path method
 - .3 Project management information system
 - .4 Resource optimization
 - .5 Leads and lags
 - .6 Schedule compression
- .3 Outputs
 - .1 Work performance information
 - .2 Schedule forecasts
 - .3 Change requests
 - .4 Project management plan updates
 - .5 Project documents updates

Knowledge Area 3 - Schedule Management

- **Purpose:** Plan and control project timelines to ensure on-time delivery.
- **Key activities:** Define activities, sequence, estimate durations, develop and control schedule.
- **IT example:** Scheduling sprints in agile development or milestones in a waterfall project.

Project Cost Management Overview

7.1 Plan Cost Management

- .1 Inputs
 - .1 Project charter
 - .2 Project management plan
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data analysis
 - .3 Meetings
- .3 Outputs
 - .1 Cost management plan

7.2 Estimate Costs

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Analogous estimating
 - .3 Parametric estimating
 - .4 Bottom-up estimating
 - .5 Three-point estimating
 - .6 Data analysis
 - .7 Project management information system
 - .8 Decision making
- .3 Outputs
 - .1 Cost estimates
 - .2 Basis of estimates
 - .3 Project documents updates

7.3 Determine Budget

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Business documents
 - .4 Agreements
 - .5 Enterprise environmental factors
 - .6 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Cost aggregation
 - .3 Data analysis
 - .4 Historical information review
 - .5 Funding limit reconciliation
 - .6 Financing
- .3 Outputs
 - .1 Cost baseline
 - .2 Project funding requirements
 - .3 Project documents updates

7.4 Control Costs


- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Project funding requirements
 - .4 Work performance data
 - .5 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data analysis
 - .3 To-complete performance index
 - .4 Project management information system
- .3 Outputs
 - .1 Work performance information
 - .2 Cost forecasts
 - .3 Change requests
 - .4 Project management plan updates
 - .5 Project documents updates

Knowledge Area 4 - Cost Management

- **Purpose:** Plan, estimate, budget, and control project costs.
- **Key activities:** Estimate costs, determine budget, control costs to prevent overruns.
- **IT example:** Managing budget for cloud infrastructure, licensing, and developer resources.

Knowledge Area 5 - Quality Management

- **Purpose:** Ensure deliverables meet defined standards and satisfy stakeholders.
- **Key activities:** Plan quality, perform quality assurance, control quality.
- **IT example:** Ensuring software passes testing and meets security/compliance standards.

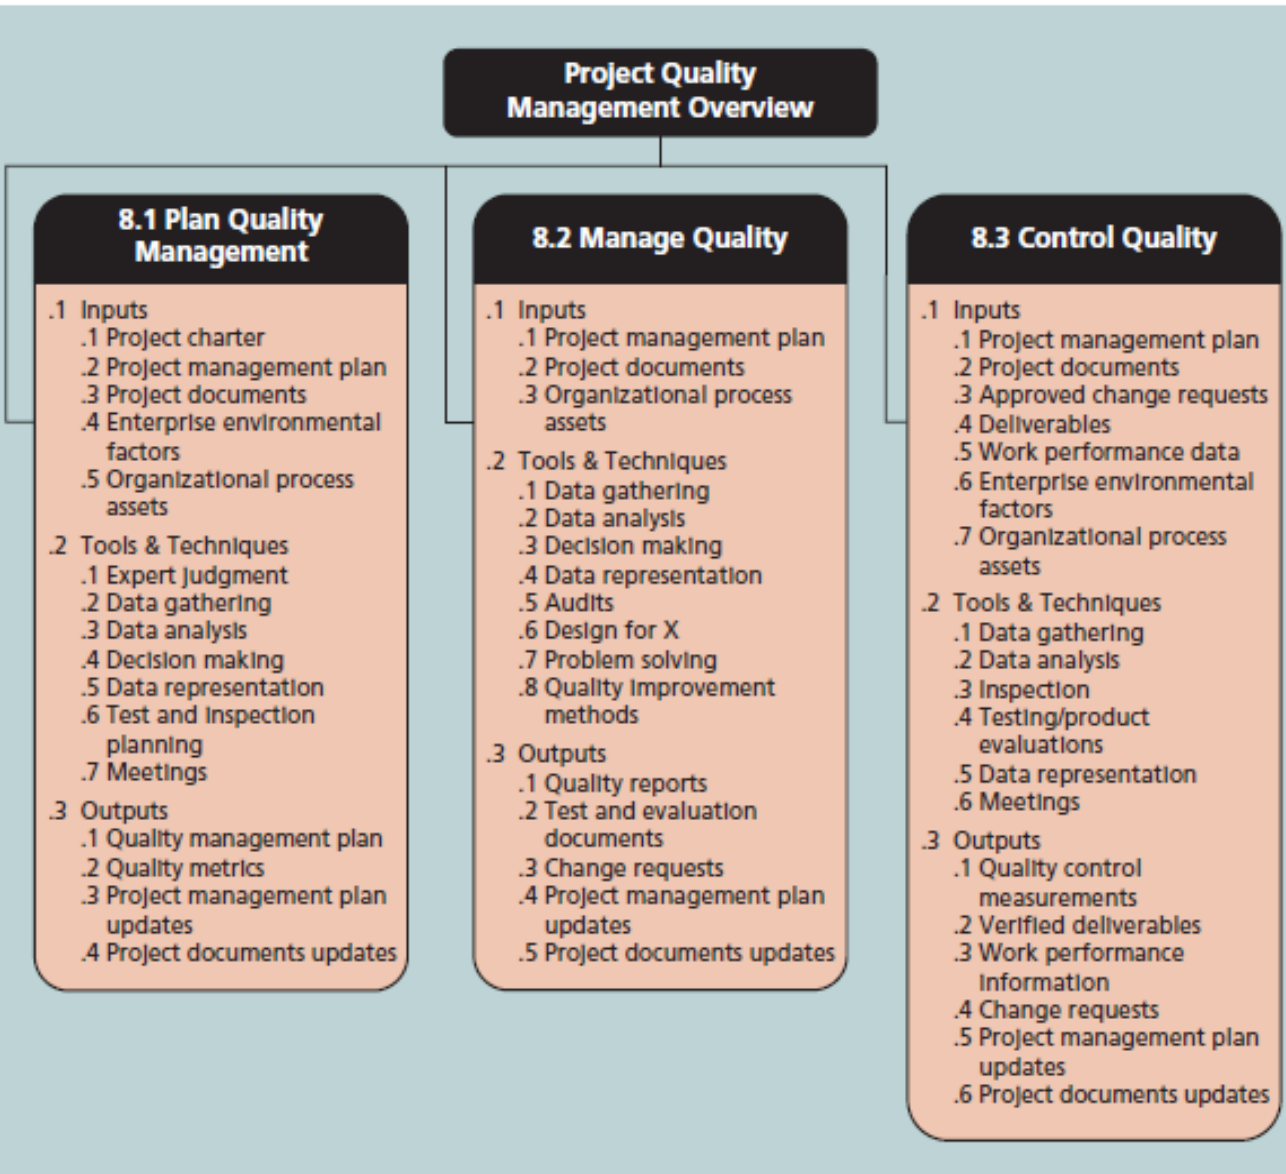

Source: *PMBOK® Guide – Sixth Edition*. Project Management Institute, Inc. (2017). Copyright and all rights reserved. Material from this publication has been reproduced with permission of PMI.

Project Resource Management Overview

9.1 Plan Resource Management

- .1 Inputs
 - .1 Project charter
 - .2 Project management plan
 - .3 Project documents
 - .4 Enterprise environmental factors
 - .5 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data representation
 - .3 Organizational theory
 - .4 Meetings
- .3 Outputs
 - .1 Resource management plan
 - .2 Team charter
 - .3 Project documents updates

9.4 Develop Team

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Colocation
 - .2 Virtual teams
 - .3 Communication technology
 - .4 Interpersonal and team skills
 - .5 Recognition and rewards
 - .6 Training
 - .7 Individual and team assessments
 - .8 Meetings
- .3 Outputs
 - .1 Team performance assessments
 - .2 Change requests
 - .3 Project management plan updates
 - .4 Project documents updates
 - .5 Enterprise environmental factors updates
 - .6 Organizational process assets updates

9.2 Estimate Activity Resources

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Bottom-up estimating
 - .3 Analogous estimating
 - .4 Parametric estimating
 - .5 Data analysis
 - .6 Project management information system
 - .7 Meetings
- .3 Outputs
 - .1 Resource requirements
 - .2 Basis of estimates
 - .3 Resource breakdown structure
 - .4 Project documents updates

9.5 Manage Team

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Work performance reports
 - .4 Team performance assessments
 - .5 Enterprise environmental factors
 - .6 Organizational process assets
- .2 Tools & Techniques
 - .1 Interpersonal and team skills
 - .2 Project management information system
- .3 Outputs
 - .1 Change requests
 - .2 Project management plan updates
 - .3 Project documents updates
 - .4 Enterprise environmental factors updates

9.3 Acquire Resources

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Decision making
 - .2 Interpersonal and team skills
 - .3 Pre-assignment
 - .4 Virtual teams
- .3 Outputs
 - .1 Physical resource assignments
 - .2 Project team assignments
 - .3 Resource calendars
 - .4 Change requests
 - .5 Project management plan updates
 - .6 Project documents updates
 - .7 Enterprise environmental factors updates
 - .8 Organizational process assets updates

9.6 Control Resources

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Work performance data
 - .4 Agreements
 - .5 Organizational process assets
- .2 Tools & Techniques
 - .1 Data analysis
 - .2 Problem solving
 - .3 Interpersonal and team skills
 - .4 Project management information system
- .3 Outputs
 - .1 Work performance information
 - .2 Change requests
 - .3 Project management plan updates
 - .4 Project documents updates

Knowledge Area 6 - Resource Management


Purpose: Plan, acquire, and manage people, equipment, and materials.

Key activities: Resource planning, estimating, acquiring, developing, and managing teams.

IT example: Assigning developers, testers, and system admins efficiently.

Knowledge Area 7 - Communication Management

- **Purpose:** Ensure timely and effective information flow.
- **Key activities:** Plan communications, manage communications, monitor communications.
- **IT example:** Reporting progress to stakeholders, updating teams on sprint progress.

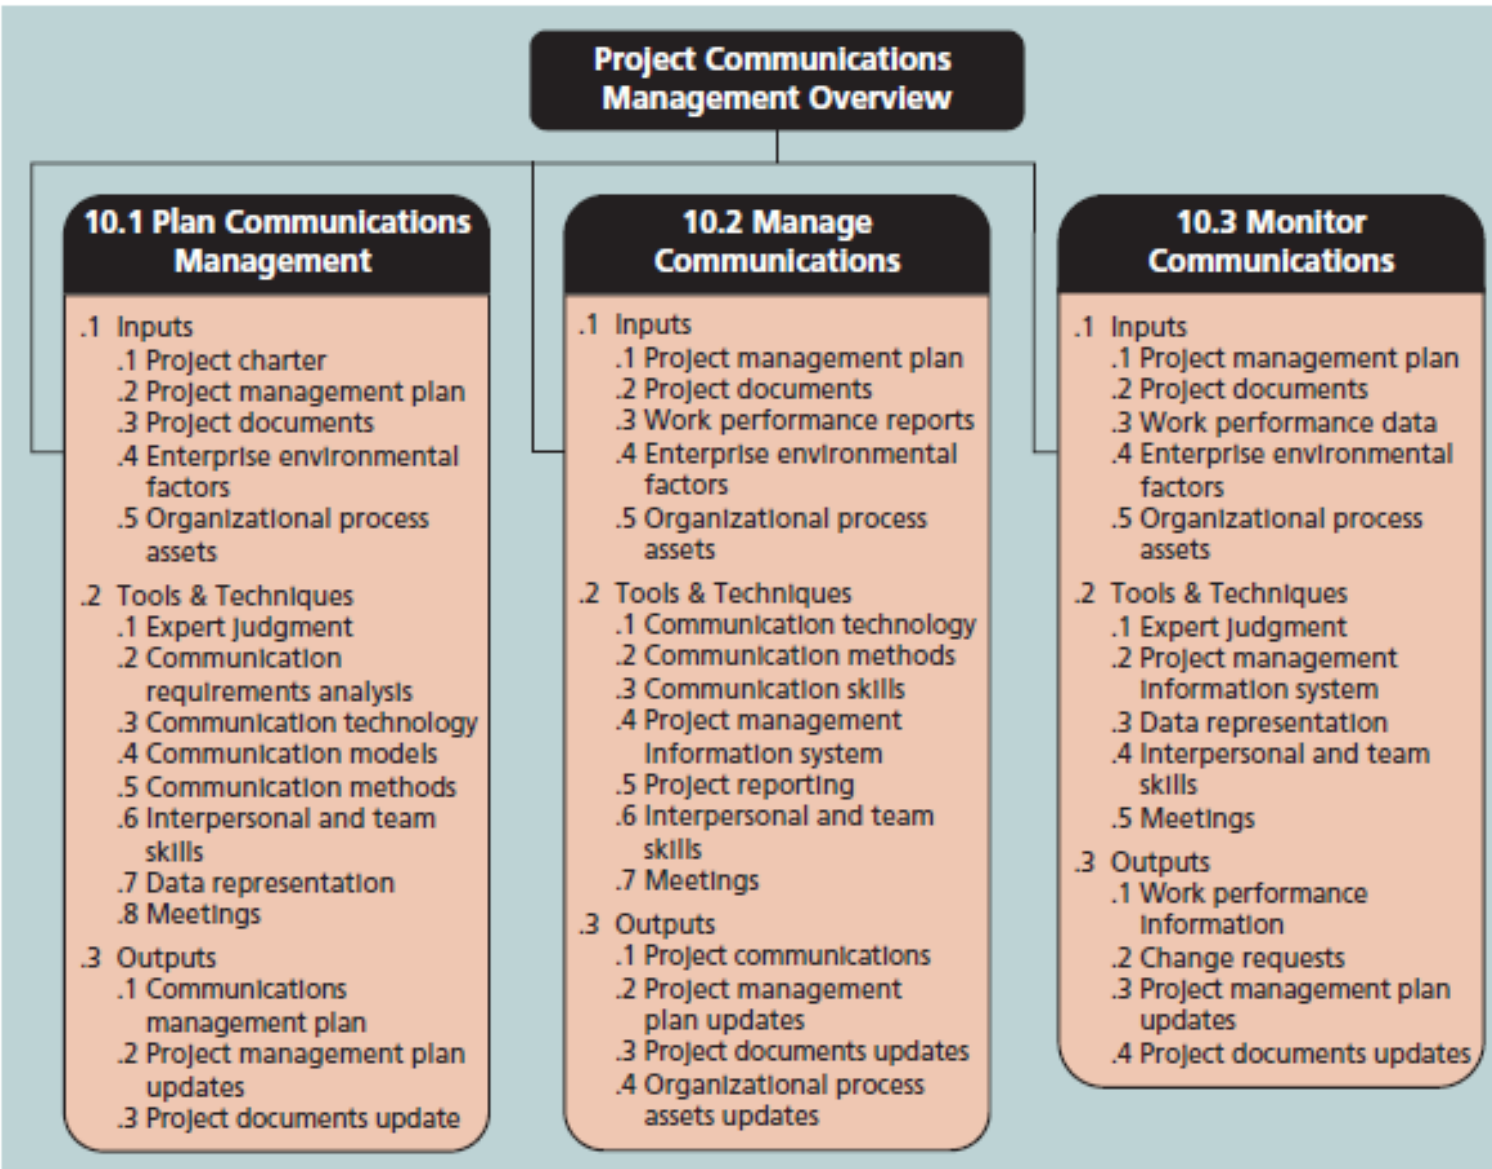

Source: *PMBOK® Guide – Sixth Edition*. Project Management Institute, Inc. (2017). Copyright and all rights reserved. Material from this publication has been reproduced with permission of PMI.

Project Risk Management Overview

11.1 Plan Risk Management

- .1 Inputs
 - .1 Project charter
 - .2 Project management plan
 - .3 Project documents
 - .4 Enterprise environmental factors
 - .5 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data analysis
 - .3 Meetings
- .3 Outputs
 - .1 Risk management plan

11.2 Identify Risks

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Agreements
 - .4 Procurement documentation
 - .5 Enterprise environmental factors
 - .6 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data gathering
 - .3 Data analysis
 - .4 Interpersonal and team skills
 - .5 Prompt lists
 - .6 Meetings
- .3 Outputs
 - .1 Risk register
 - .2 Risk report
 - .3 Project documents updates

11.3 Perform Qualitative Risk Analysis

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data gathering
 - .3 Data analysis
 - .4 Interpersonal and team skills
 - .5 Risk categorization
 - .6 Data representation
 - .7 Meetings
- .3 Outputs
 - .1 Project documents updates

11.4 Perform Quantitative Risk Analysis

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data gathering
 - .3 Interpersonal and team skills
 - .4 Representations of uncertainty
 - .5 Data analysis
- .3. Outputs
 - .1 Project documents updates

11.5 Plan Risk Responses

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Enterprise environmental factors
 - .4 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data gathering
 - .3 Interpersonal and team skills
 - .4 Strategies for threats
 - .5 Strategies for opportunities
 - .6 Contingent response strategies
 - .7 Strategies for overall project risk
 - .8 Data analysis
 - .9 Decision making
- .3 Outputs
 - .1 Change requests
 - .2 Project management plan updates
 - .3 Project documents updates

11.6 Implement Risk Responses

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Interpersonal and team skills
 - .3 Project management information system
- .3 Outputs
 - .1 Change requests
 - .2 Project documents updates

11.7 Monitor Risks

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Work performance data
 - .4 Work performance reports
- .2. Tools & Techniques
 - .1 Data analysis
 - .2 Audits
 - .3 Meetings
- .3. Outputs
 - .1 Work performance information
 - .2 Change requests
 - .3 Project management plan updates
 - .4 Project documents updates
 - .5 Organizational process assets updates

Knowledge Area 8 - Risk Management

- **Purpose:** Identify, analyze, and mitigate project risks.
- **Key activities:** Risk identification, qualitative & quantitative analysis, risk response planning, risk monitoring.
- **IT example:** Planning for potential server downtime, security breaches, or requirement changes.

Project Procurement Management Overview

12.1 Plan Procurement Management

- .1 Inputs
 - .1 Project charter
 - .2 Business documents
 - .3 Project management plan
 - .4 Project documents
 - .5 Enterprise environmental factors
 - .6 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Data gathering
 - .3 Data analysis
 - .4 Source selection analysis
 - .5 Meetings
- .3 Outputs
 - .1 Procurement management plan
 - .2 Procurement strategy
 - .3 Bid documents
 - .4 Procurement statement of work
 - .5 Source selection criteria
 - .6 Make-or-buy decisions
 - .7 Independent cost estimates
 - .8 Change requests
 - .9 Project documents updates
 - .10 Organizational process assets updates

12.2 Conduct Procurements

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Procurement documentation
 - .4 Seller proposals
 - .5 Enterprise environmental factors
 - .6 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Advertising
 - .3 Bidder conferences
 - .4 Data analysis
 - .5 Interpersonal and team skills
- .3 Outputs
 - .1 Selected sellers
 - .2 Agreements
 - .3 Change requests
 - .4 Project management plan updates
 - .5 Project documents updates
 - .6 Organizational process assets updates

12.3 Control Procurements

- .1 Inputs
 - .1 Project management plan
 - .2 Project documents
 - .3 Agreements
 - .4 Procurement documentation
 - .5 Approved change requests
 - .6 Work performance data
 - .7 Enterprise environmental factors
 - .8 Organizational process assets
- .2 Tools & Techniques
 - .1 Expert judgment
 - .2 Claims administration
 - .3 Data analysis
 - .4 Inspection
 - .5 Audits
- .3 Outputs
 - .1 Closed procurements
 - .2 Work performance information
 - .3 Procurement documentation updates
 - .4 Change requests
 - .5 Project management plan updates
 - .6 Project documents updates
 - .7 Organizational process assets updates

Knowledge Area 9 - Procurement Management

- **Purpose:** Acquire goods, services, or results from external sources.
- **Key activities:** Plan procurement, conduct procurement, control procurement, close procurement.
- **IT example:** Hiring cloud service providers or purchasing software licenses.

Exam Overview

Quick Recap

- Total time for the exam: **2 hours 10 minutes**
- Reading time: **10 minutes**
- Writing time: **2 hours**
- **Total Marks: 50**
- Format:
 - **10 MCQ questions**
 - **3 Short Answer questions**
 - **Has 3 to 4 sub-questions**

Allowed Materials

- ONE A4 size sheet
- Handwritten or Printed on BOTH sides
- Bilingual dictionary

Types of questions in Short Answer based

- Explanations with examples
- Differences with examples
- Scenario based questions
- Calculation based questions
- How to get maximum marks?
 - Be as descriptive as possible but to the point!
 - We do not want to see the exact points mentioned in the slides.
 - We want to see your explanation, your understanding of the concepts!

How should you prepare for the exam?

- Understand the CONCEPTS!
- Exam preparation help from the teaching team:
 - Lecture slides
 - Tutorial sheets
 - Lecture recordings
 - Ed Forum – To clarify any concepts!
 - **Exam Support sessions will be there till week 14**
 - Practice exam papers

Marking Guide

You will be awarded **marks for attempting the questions** in Part B (Scenario-Based Section).

Please do not leave any answers blank, a minimum mark will be awarded for each attempted question.

Important topics

WK	Topic
Week 01	Introduction to IT project management
Week 02	IT Project Methods and Requirements Gathering Strategies
Week 03	IT Project Time: Tools, Techniques, Real-world Case Study
Week 04	IT Project Cost: Tools, Techniques, Real-world Case Study
Week 05	IT Project Quality: Tools, Techniques, Real-world Case Study
Week 06	IT Project Resources: Tools, Techniques, Real-world Case Study
Week 07	Knowledge test
Week 08	IT Project Risk: Tools, Techniques, Real-world Case Study
Week 09	IT Project Outsourcing and Procurement Strategy
Week 10	IT Project Leadership, Governance, and Alignment
Week 11	IT service management functions and processes & IT Project in Different Industries: Presentation 1
Week 12	IT service management functions and processes & IT Project in Different Industries: Presentation 2

Syllabus

- Each question covers a major topic covered throughout the semester.

Week 1 - Introduction

- What is a project?
- Difference between Project, Program and Portfolio Management
- Factors influencing Project Success
- Project Management Knowledge Areas

Week 2 – PM Methodologies

- Project Lifecycle
- Waterfall Model
- Agile Model
- DevOps
- Requirement gathering

Week 3 – Schedule Management Plan

- Project Scope Management processes
- Project Schedule Management processes
- Network Diagrams
- Controlling Scope
- Controlling Schedule

Week 4 – Cost Management Plan

- What are the different types of costs
- Cost management processes
- Earned Value Management
- Controlling Costs

Week 5 – Quality Management Plan

- What is Quality?
- Quality management processes
- Tools and techniques used in Quality management
- Deming and his 14 points for management
- Cost of quality and trade-offs
- Controlling quality

Week 6 – Resource Management Plan

- Resource management processes
- Motivation theories
- Techniques for estimating activity resources
- Resource loading and Resource leveling
- Developing and motivating teams
- Conflict management

Week 7 – Risk Management Plan

- Types of risks
- Risk appetite
- Risk management processes
- Assessing risks
- Risk responses and controlling risks

Week 8 – Procurement Management Plan

- Procurement management processes
- Controlling procurements
- Types of Contracts
- Project outsourcing

Week 9 – Project Leadership, Governance and Alignment

- Project leadership vs Project management
- Types of leadership styles
- Project communication processes
- IT Project governance
- Alignment in IT Projects

Week 10 – Integration Management

- Characteristics of IT projects
- How do the different knowledge areas integrate with each other?

Week 11 – ITSM and Processes 1

- What is ITSM
- Products and Services in IT
- Service Relationship models
- What is ITIL v4.0?
- Components of ITIL v4.0

Week 12 – ITSM and processes 2

- ITIL v4.0 in detail
- Key Service practices
 - Incident management
 - Problem management
 - Change management
 - Service Level management
 - Service desk
 - Continual improvements

USS Feedback



We Value Your Feedback!

Your feedback helps us improve the learning experience for current and future students.

What We Have Done This Semester:

- Redesigned lecture slides to make content more engaging and easier to follow.
- Improved tutorial materials with more practical examples and discussion-based activities.
- Introduced industry guest lectures to connect classroom learning with real-world practice.
- Enhanced assessment clarity and alignment with learning outcomes.
- Created a more inclusive and supportive learning environment for all students.
- Provided personalised guidance and regular updates through SRES and Ed Discussion.

Unit of Study Survey

- Your feedback is extremely valuable!!
- Closes on: Saturday, 7 June



<https://student-surveys.sydney.edu.au/s/uss985123>

Best Participant Award – Tutorial Engagement 🏆 🎉



And finally – the best participant for INFO6007 in Sem 1, 2026

We are delighted to recognise students who have shown exceptional engagement, collaboration, and enthusiasm during tutorial sessions this semester.

The top students are picked by the tutors.

Award Criteria:

- Active and consistent participation in tutorials.
- Constructive contributions to discussions and group activities.
- Supportive and respectful collaboration with peers.
- Positive attitude and professionalism throughout the semester.


E-Certificates will be sent shortly to all award recipients. Please check your student email for details.

Final Reminders – Exam Support

This is our **last lecture**, but the **teaching team is still available** to support you.

- **Exam support sessions** will continue until **5th June (next week)**.
- If you'd like a **one-to-one consultation**, please **book an appointment** by emailing:
mowrin.hossain@sydney.edu.au
- Make sure to **review the practice questions** shared earlier.
- If you need any help, please **contact your tutor** or reach out to the teaching team.

Thank you all for the wonderful semester!



THE UNIVERSITY OF
SYDNEY
